



Certificate of Compliance

Customer: Downhole & Design

Date: 02-18-2026

Material Description: 4.000" X 2.720" 13CR80 TUBE

PO# PO001988

Part# 4.000X2.720-ES-M0003E

Heat# F517124

Lot # 001

Batch# N/A

Customer Specification/Rev: ES-M0003E REV 0

Hardness: 235/229

Comments: 1 PC 208.50, 1 PC 208.375" LG

SAS hereby certifies that the material described above and on the attached test report and inspection complies with the purchase order contract, as agreed upon.

This order was processed in accordance with the latest revision of the SAS Quality Manual conforming to ISO9001:2015; APIQ1 & API20J DQL 2 requirements.

Signature: *Carrie Henry*

Printed Name: Carrie Henry

Title: Office Manager

F517124-1988

**NIPPON STEEL**NIPPON STEEL CORPORATION
KANSAI WORKS WAKAYAMA AREA (KAINAN)
260-100, FUNOO, KAINAN, JAPAN

INSPECTION CERTIFICATE

CERTIFICATE NO. :BYVF3788-01 PAGE : 1/4 DATE :2025-11-26

CUSTOMER :STEEL ALLOYS & SERVICES

ORDER NO. :P. O. NO. 31716

SHIPPER :KANEMATSU CORPORATION 026 TEJ52-EJ52-0499 5-845-N3-5-0-WK50-01

COMMODITY :SEAMLESS HOT FINISHED STEEL PIPE

STANDARD :API 5CT GR. L80-TYPE 13CR(11TH ED., DEC. 2023)

SPECIFICATION :TSP-5759R2

MILL WORK NO. :BYVF3788

O. D. :4.000in. W. T. :0.640in. LENGTH:MIN. 20.0ft MAX. 37.0ft
QUANTITY:56pcs. TOTAL LENGTH:1927.55ft MASS:19873kg (43813lbs)

HEAT NO. :F517124

PRODUCTS PCS. :56

HEAT TREATMENT :QUENCHED & TEMPERED

CHEMICAL COMPOSITION(%)

		C	Si	Mn	P	S	Cu	Cr	Ni	Mo	Nb	Al
	#1	#2 #3										
SPEC. MIN.	L	18	-	25	-	-	-	120	-	-	-	-
MAX.	L	22	100	100	20	10	25	140	50	-	-	-
MIN.	P	15	-	25	-	-	-	120	-	-	-	-
MAX.	P	22	100	100	20	10	25	140	50	-	-	-
HEAT NO.												
F517124	L	19	25	52	13	1	1	129	10	1	0	4
	P	18	24	52	13	1	2	128	10	1	0	6
	P	18	24	53	14	1	2	127	10	1	0	6
*1 L:LADLE ANALYSIS P:PRODUCT ANALYSIS *2:X10 *3:X1000 OTHER:X100												

TENSILE TEST

		YS	TS	EL	RA
	#1 #2	#3	#3	%	%
SPEC. MIN.	L B	P 80.0	P 100.0	18	-
MAX.	L B	P 95.0	P 120.0	-	-
HEAT NO.					
F517124	L B	P 84.4	P 108.8	26	71
	L B	P 85.3	P 110.2	26	71

TYPE OF SPECIMEN:ROUND BAR 0.35in. DIAMETER *1 SAMPLING DIRECTION L:LONGITUDINAL

*2 SAMPLING POSITION B:BASE METAL *3 UNIT P:ksi GAUGE LENGTH:1.4in. KIND OF YS:0.5% EXTENSION UNDER LOAD

TENSILE TEST

		YS	TS	EL	RA
	#1 #2	#3	#3	%	%
SPEC. MIN.	L B	P 80.0	P 100.0	18	-
MAX.	L B	P 95.0	P 120.0	-	-
HEAT NO.					
F517124	L B	P 83.0	P 108.6	27	72
	L B	P 84.7	P 110.4	26	71

THE PRODUCT HAS BEEN MANUFACTURED, SAMPLED, TESTED AND/OR INSPECTED IN ACCORDANCE WITH THIS DOCUMENT (*1)
AND HAS BEEN FOUND TO MEET THE REQUIREMENTS.

*1) THIS DOCUMENT MEANS "STANDARD" THAT APPLIES TO THIS INSPECTION CERTIFICATE.

T. Inui

TOSHIKAZU INUI

HEAD OF DEPARTMENT, KANSAI QUALITY MANAGEMENT DEPT.
QUALITY MANAGEMENT DIV.<Notice>
Modification to or unauthorized use of this certificate is strictly prohibited. If you have any questions on the authenticity of this certificate, you can contact us by E-mail, pipe-ipp@jp.nipponsteel.com .
NO. 652086K25

F517124-1988



NIPPON STEEL CORPORATION
KANSAI WORKS WAKAYAMA AREA (KAINAN)
260-100, FUNOO, KAINAN, JAPAN

INSPECTION CERTIFICATE

CERTIFICATE NO. :BYFF3788-01 PAGE : 2/4 DATE :2025-11-26

TYPE OF SPECIMEN:ROUND BAR 0.35in. DIAMETER *1 SAMPLING DIRECTION L:LONGITUDINAL
*2 SAMPLING POSITION B:BASE METAL *3 UNIT P:ksi GAUGE LENGTH:1.4in. KIND OF YS:0.2% OFFSET

IMPACT TEST(+32.0°F 2mm V-Notch 10X5.00)

SPEC. MIN. MAX.	HEAT- LOT NO.	*1 *2		*3 *4		AVG		*3 *4		AVG		AVG	
		T B	E F	*5	7/11	11	S %	S %	*6	-	-	-	-
		T B	E F		-/-	-	S %			-	-	-	-
		[1]	[2]	[3]					[1]	[2]	[3]		
HEAT NO. F517124	001	T B	E F	39	42	46	42	S %	89	89	100	93	

[1] [2] [3]: SPECIMEN NO.

ABSORBED ENERGY

*5:ABSOLUTE SINGLE VALUE / SINGLE VALUE (ONE CAN BE BELOW AVG) AVG:AVERAGE VALUE OF ONE SET (3 PIECES)
SHEAR AREA *6:VALUE OF ONE PIECE AVG:AVERAGE VALUE OF ONE SET (3 PIECES)
*1 SAMPLING DIRECTION T:TRANSVERSE *2 SAMPLING POSITION B:BASE METAL *3 E:ABSORBED ENERGY S:SHEAR AREA
*4 UNIT F:ft·lbf %:%

IMPACT TEST(+14.0°F 2mm V-Notch 10X10)

SPEC. MIN. MAX.	HEAT- LOT NO.	*1 *2		*3 *4		AVG		*3 *4		AVG		AVG	
		L B	E F	*5	15/22	22	S %	S %	*6	-	-	-	-
		L B	E F		-/-	-	S %			-	-	-	-
		[1]	[2]	[3]					[1]	[2]	[3]		
HEAT NO. F517124	001	L B	E F	83	87	83	84	S %	48	49	47	48	

[1] [2] [3]: SPECIMEN NO.

ABSORBED ENERGY

*5:ABSOLUTE SINGLE VALUE / SINGLE VALUE (ONE CAN BE BELOW AVG) AVG:AVERAGE VALUE OF ONE SET (3 PIECES)
SHEAR AREA *6:VALUE OF ONE PIECE AVG:AVERAGE VALUE OF ONE SET (3 PIECES)
*1 SAMPLING DIRECTION L:LONGITUDINAL *2 SAMPLING POSITION B:BASE METAL *3 E:ABSORBED ENERGY S:SHEAR AREA
*4 UNIT F:ft·lbf %:%

FERRITE CONTENT TEST (DELTA FERRITE RATIO) (%)

SPEC. MIN. MAX.	HEAT- LOT NO.				
				4.99	
HEAT NO. F517124	001			0	

MICRO STRUCTURE TEST: ACCEPTABLE (REFER TO ATTACHED SHEET)

VISUAL & DIMENSIONS: ACCEPTABLE

ULTRASONIC EXAMINATION: ACCEPTABLE

APPLICABLE STANDARD: API 5CT

REFERENCE STANDARD: L2 EXTERNAL LONGITUDINAL & TRANSVERSE NOTCH LENGTH 2.0in.

INTERNAL LONGITUDINAL & TRANSVERSE NOTCH LENGTH 1.0in. WIDTH 0.040in.

ULTRASONIC EXAMINATION (LAMINATION) : ACCEPTABLE

REFERENCE STANDARD: 0.25in. FLAT BOTTOMED ROUND HOLE

ULTRASONIC WALL THICKNESS CHECK: ACCEPTABLE

SEAMLESS (BILLET SHALL BE MADE FINE GRAIN PRACTICE)

THE PRODUCT HAS BEEN MANUFACTURED, SAMPLED, TESTED AND/OR INSPECTED IN ACCORDANCE WITH THIS DOCUMENT (*1)
AND HAS BEEN FOUND TO MEET THE REQUIREMENTS.

*1) THIS DOCUMENT MEANS "STANDARD" THAT APPLIES TO THIS INSPECTION CERTIFICATE.

T. Inui TOSHIKAZU INUI

HEAD OF DEPARTMENT, KANSAI QUALITY MANAGEMENT DEPT.
QUALITY MANAGEMENT DIV.

<Notice>

Modification to or unauthorized use of this certificate is strictly prohibited. If you have any questions on the authenticity of this certificate, you can contact us by E-mail, pipe-ipp@jp.nipponsteel.com.

NO. 652086K25

F517124-1988



NIPPON STEEL

NIPPON STEEL CORPORATION
KANSAI WORKS WAKAYAMA AREA (KAINAN)
260-100, FUNOO, KAINAN, JAPAN

INSPECTION CERTIFICATE

CERTIFICATE NO. : BYVF3788-01 PAGE : 3/4 DATE : 2025-11-26

WE HEREBY CERTIFY THAT EACH PIPE HAS BEEN MARKED WITH THE HEAT NUMBER AND TRACEABLE ON EVERY PIPE.
DIMENSION AND WEIGHT TESTS INCLUDING DRIFT TEST AND STRAIGHTNESS: ACCEPTABLE
NO REPAIR BY WELDING.

MELTED AND MANUFACTURED IN JAPAN

MELTED/CASTED (POURED) /MANUFACTURED IN JAPAN

PRIMARY MELTING METHOD: BOF

MELTING PRACTICE: AOD AND/OR VOD

SAMPLING LOCATION OF ROUND BAR TENSILE TEST: MID-WALL

EN 10204 3.1

THE PRODUCT HAS BEEN MANUFACTURED, SAMPLED, TESTED AND/OR INSPECTED IN ACCORDANCE WITH THIS DOCUMENT (*1)
AND HAS BEEN FOUND TO MEET THE REQUIREMENTS.
*1) THIS DOCUMENT MEANS "STANDARD" THAT APPLIES TO THIS INSPECTION CERTIFICATE.

T. Inui

TOSHIKAZU INUI

HEAD OF DEPARTMENT, KANSAI QUALITY MANAGEMENT DEPT.
QUALITY MANAGEMENT DIV.

<Notice>
Modification to or unauthorized use of this certificate is strictly prohibited. If you have any questions on the authenticity of this certificate, you can contact us by E-mail, pipe-ipp@jp.nipponsteel.com .
NO. 652086K25

F517124-1988



NIPPON STEEL

NIPPON STEEL CORPORATION
KANSAI WORKS WAKAYAMA AREA (KAINAN)
260-100, FUNOO, KAINAN, JAPAN

INSPECTION CERTIFICATE

CERTIFICATE NO. :BYVF3788-01 PAGE : 4/4 DATE :2025-11-26

HARDNESS TEST(HRC)

		*1*2	*3	*4	*5	*V. A.												
SPEC. MIN.		B C		-	16.0	-												
	MAX.	B C		24.0	22.0	-												
		AVG.																
HEAT NO.	HEAT- LOT NO.	OUTER WALL		MID WALL		INNER WALL												
		IMPRESSION NO.		IMPRESSION NO.														
		QUAD		-RANT														
		(1)	(2)	(3)	AVG.	(1)	(2)	(3)	AVG.									
F517124	001	B C	T	20.0	A	19.7	20.2	19.8	19.9	20.1	20.3	20.2	19.9	19.9	20.1	20.0	0.3	
	001	B C	B	20.3	A	20.1	20.3	20.4	20.3	20.4	20.8	20.6	20.6	20.3	20.1	19.7	20.0	0.6
				*ALL	20.2													
*1 SAMPLING POSITION B:BASE METAL *2 LOCATION C:CROSS SECTION *3 SAMPLING LOCATION T:TOP B:BOTTOM *4 EACH																		
*5 AVERAGE *V. A.: VARIATION AVERAGE MAX.-MIN. * ALL:ALL AVG.																		

THE PRODUCT HAS BEEN MANUFACTURED, SAMPLED, TESTED AND/OR INSPECTED IN ACCORDANCE WITH THIS DOCUMENT(*1)
AND HAS BEEN FOUND TO MEET THE REQUIREMENTS.
*1) THIS DOCUMENT MEANS "STANDARD" THAT APPLIES TO THIS INSPECTION CERTIFICATE.

T. Inui TOSHIKAZU INUI

HEAD OF DEPARTMENT, KANSAI QUALITY MANAGEMENT DEPT.
QUALITY MANAGEMENT DIV.

<Notice>
Modification to or unauthorized use of this certificate is strictly prohibited. If you have any questions on the authenticity of this certificate, you can contact us by E-mail, pipe-ipp@jp.nipponsteel.com .
NO. 652086K25



NIPPON STEEL

NIPPON STEEL CORPORATION
KANSAI WORKS WAKAYAMA AREA (KAINAN)
260-100, FUNOO, KAINAN, JAPAN

ATTACHED SHEET

F517124-1988


CERTIFICATE NO. :BYVF3788-01

PAGE : 1/1

DATE : 2025-11-26

MICRO STRUCTURE TEST

X100

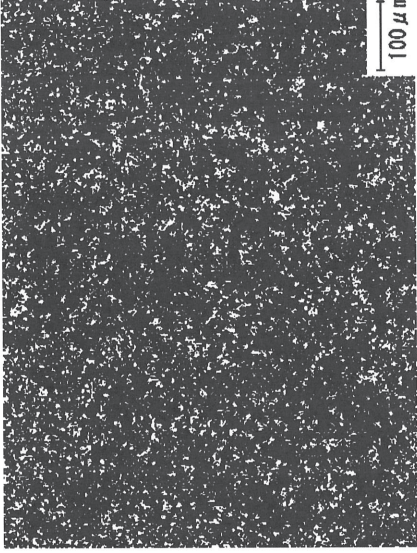

100 μ m

HEAT NO. :F517124
HEAT-
LOT NO. :001

T. Inui

TOSHIKAZU INUI

HEAD OF DEPARTMENT, KANSAI QUALITY MANAGEMENT DEPT.
QUALITY MANAGEMENT DIV.

NO. 652086K25



NIPPON STEEL

1850, MINATO, WAKAYAMA, JAPAN

NIPPON STEEL CORPORATION

KANSAI WORKS

TEL No. (KANSAI) 81-73-451-3977

FAX No. (KANSAI) 81-73-452-7065

25648WR0

Date: 05-Dec-25

To: STEEL ALLOYS & SERVICES

NIPPON STEEL Corporation, who are established and reputable manufacturers of OCTG having factories at 1850, Minato-Wakayama-shi, Wakayama, Japan, certify that the products on the following Inspection Certificate No. are manufactured in accordance with the descriptions below.

Inspection Certificate No.

BYZF3788

CUSTOMER:

STEEL ALLOYS & SERVICES

ORDER NO.:

31716

Grade:

L80-13CR

Size:

4.000 x 0.640

Ex-mill:

20-Oct-25

- | | |
|--|---------------|
| • Austenitizing Time (Q-Furnace Soaking Time): | Min. 32 min |
| • Austenitizing Temperature: | 950 deg.C |
| • Quenchant: | Air Quenching |
| • Tempering Time: | Min. 41 min |
| • Tempering Temperature: | 700 deg.C |
| • Cooling Method: | Air Cooling |

Shunichi Kobayashi

Senior Manager, Head of Section

OCTG Technical Service & Solution Section

OCTG & Line Pipe Products Technical Service & Solution Dept.

Pipe & Tube Unit Tubular Products Technology Div.

NIPPON STEEL CORPORATION
